

月間工程表

工事名称 六和クリーンセンター解体工事
 施工 前田建設工業(株) 松戸六和CC解体作業所


[平成31年4月1日～平成31年4月30日]

3月末予定進捗率 95%

3月末進捗率 95%

工事種類	2019年																																備考											
	3月							4月																										5月										
	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25		26	27	28	29	30	1	2	3	4		
月	火	水	木	金	土	日	月	火	水	木	金	土	日	月	火	水	木	金	土	日	月	火	水	木	金	土	日	月	火	水	木	金	土	日	月	火	水	木	金	土				
仮設工事																																												
外構工事																																												
整地																																												
仮設道路																																												
産業廃棄物																																												
特管物																																												
特殊車両搬出入																																												
搬出入車両台数																																												
行事他																																												

GW休暇(4/28～5/6)

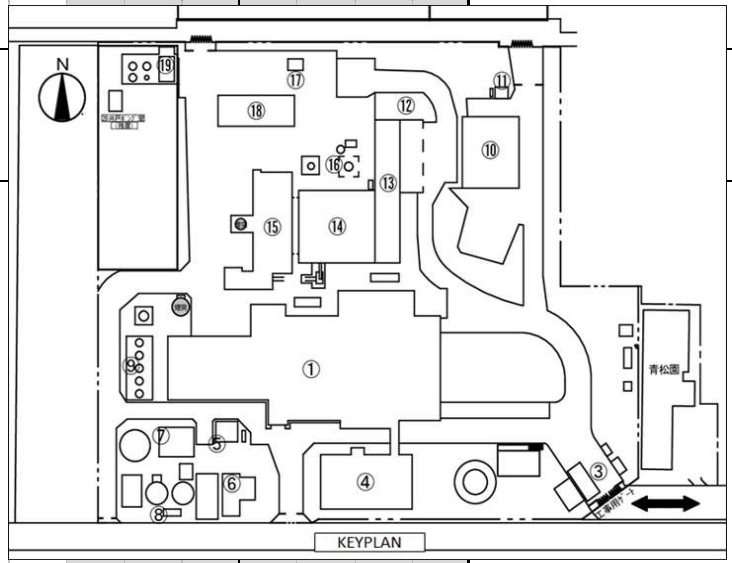

※行事凡例 定会:定例会議 災防:災害防止協議会 特安:特別安全朝礼 店社:店社バナーロール
